

ID		Task Mode	Task Name	Duration	Start	Finish	13 Nov '17							20 Nov '17							27 Nov '17																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																												
							S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									
1			HOTEL "MIRJAM" MAKARSKA	166 days	Mon 13.11.17	Sat 30.6.18																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											</

Project: Dinamički plan hotela Mir
Date: Mon 27.11.17

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

ID		Task Mode	Task Name	Duration	Start	Finish	13 Nov '17							20 Nov '17							27 Nov '17		
							S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T
23			ploča iznad II kata dilatacije A	6 days	Mon 12.2.18	Mon 19.2.18																	
24			zidovi nadgrađa	5 days	Tue 20.2.18	Sat 24.2.18																	
25			ploča iznad nadgrađa	4 days	Fri 23.2.18	Wed 28.2.18																	
26			podložni beton dilatacije b	1 day	Mon 8.1.18	Mon 8.1.18																	
27			hidroizolacija podne ploče dilatacije B	1 day	Tue 9.1.18	Tue 9.1.18																	
28			podna ploča dilatacije B	5 days	Wed 10.1.18	Tue 16.1.18																	
29			zidovi podruma 2 dilatacija B	6 days	Wed 17.1.18	Wed 24.1.18																	
30			ploča iznad podruma 2	6 days	Mon 22.1.18	Mon 29.1.18																	
31			zidovi prizemlja dilatacije B	6 days	Tue 30.1.18	Tue 6.2.18																	
32			ploča iznad prizemlja dilatacije B	5 days	Thu 1.2.18	Wed 7.2.18																	
33			zidovi I kata dilatacije B	6 days	Thu 8.2.18	Thu 15.2.18																	
34			ploča iznad I kata dilatacije B	7 days	Sat 10.2.18	Sat 17.2.18																	
35			zidovi II kata dilatacije B	6 days	Mon 19.2.18	Mon 26.2.18																	
36			ploča iznad II kata filatacije B	8 days	Wed 21.2.18	Fri 2.3.18																	
37			izrada parapetnih zidova po krovu	5 days	Sat 3.3.18	Thu 8.3.18																	
38			betoniranje bazenske školjke	10 days	Mon 12.3.18	Fri 23.3.18																	
39			izrada ogradnih zidova	9 days	Mon 26.2.18	Thu 8.3.18																	
40			izrada estriha	39 days	Thu 1.3.18	Tue 24.4.18																	
41			HIDROIZOLATERSKI RADOVI																				
42			hidroizolacija zidova podruma 1	6 days	Wed 3.1.18	Wed 10.1.18																	
43			hidroizolacija zidova podruma 2	12 days	Wed 10.1.18	Thu 25.1.18																	
44			izrada ravnog krova	11 days	Mon 26.3.18	Sat 7.4.18																	
45			hidroizolacija kupaonica	41 days	Thu 8.3.18	Thu 3.5.18																	
46			hidroizolacija terasa	43 days	Thu 8.3.18	Sat 5.5.18																	


Project: Dinamički plan hotela Mir
Date: Mon 27.11.17

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

ID		Task Mode	Task Name	Duration	Start	Finish	13 Nov '17							20 Nov '17							27 Nov '17		
							S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T
47			ZIDARSKI RADOVI																				
48			zidanje pregradnih zidova	32 days	Fri 2.2.18	Sat 17.3.18																	
49			žbukanje zidova I stropova	43 days	Wed 14.2.18	Fri 13.4.18																	
50			izrada fasade	50 days	Mon 2.4.18	Fri 8.6.18																	
51			VANJSKA STOLARIJA	17 days	Thu 1.3.18	Fri 23.3.18																	
52			INSTALACIJE																				
53			I faza	71 days	Fri 1.12.17	Fri 9.3.18																	
54			II faza	36 days	Mon 5.2.18	Sat 24.3.18																	
55			montaža I ispitivanje	57 days	Sat 31.3.18	Sat 16.6.18																	
56			GIPSKARTONSKI RADOVI																				
57			zidovi	49 days	Mon 19.2.18	Thu 26.4.18																	
58			stropovi	18 days	Mon 12.3.18	Wed 4.4.18																	
59			KERAMIČARSKI RADOVI	61 days	Mon 19.3.18	Sun 10.6.18																	
60			MOLERSKI RADOVI	35 days	Mon 26.3.18	Fri 11.5.18																	
61			PODOPOLAGAČKI RADOVI	35 days	Mon 16.4.18	Fri 1.6.18																	
62			BRAVARSKI RADOVI	13 days	Tue 15.5.18	Thu 31.5.18																	
63			UGRADNJA LIFTOVA	29 days	Mon 2.4.18	Thu 10.5.18																	
64			MONTAŽA NAMJEŠTAJA	36 days	Fri 4.5.18	Fri 22.6.18																	
65			UREĐIVANJE OKOLIŠA	15 days	Fri 1.6.18	Thu 21.6.18																	
66			ZAVRŠNO ČIŠĆENJE	8 days	Thu 21.6.18	Sat 30.6.18																	

Project: Dinamički plan hotela Mir
Date: Mon 27.11.17


Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

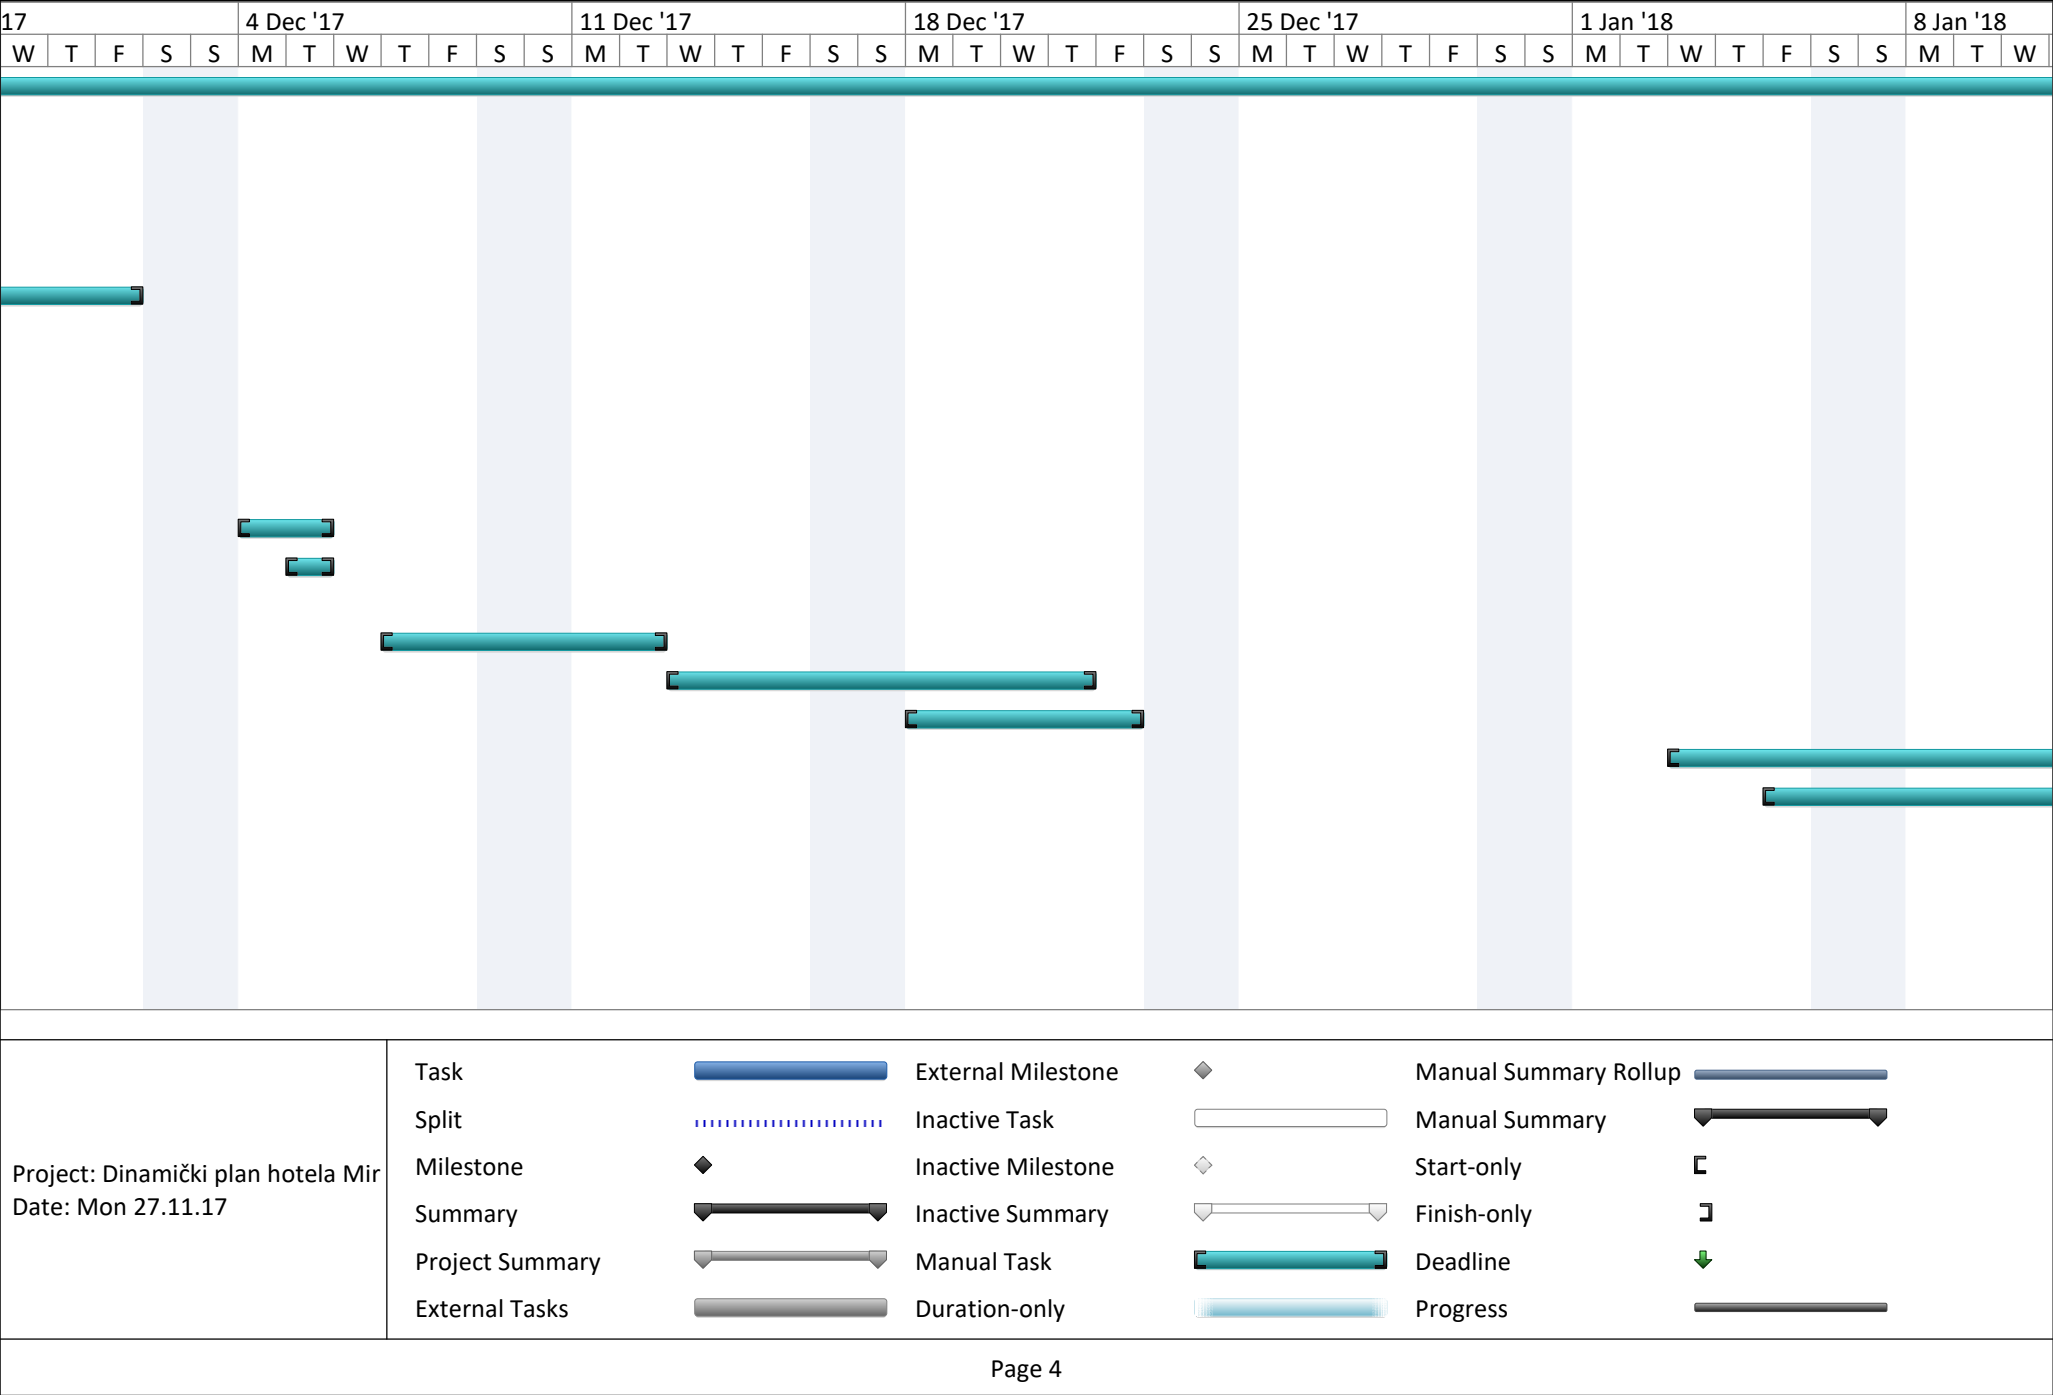



Page 4

[illegible]

Project: Dinamički plan hotela Mir Date: Mon 27.11.17	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

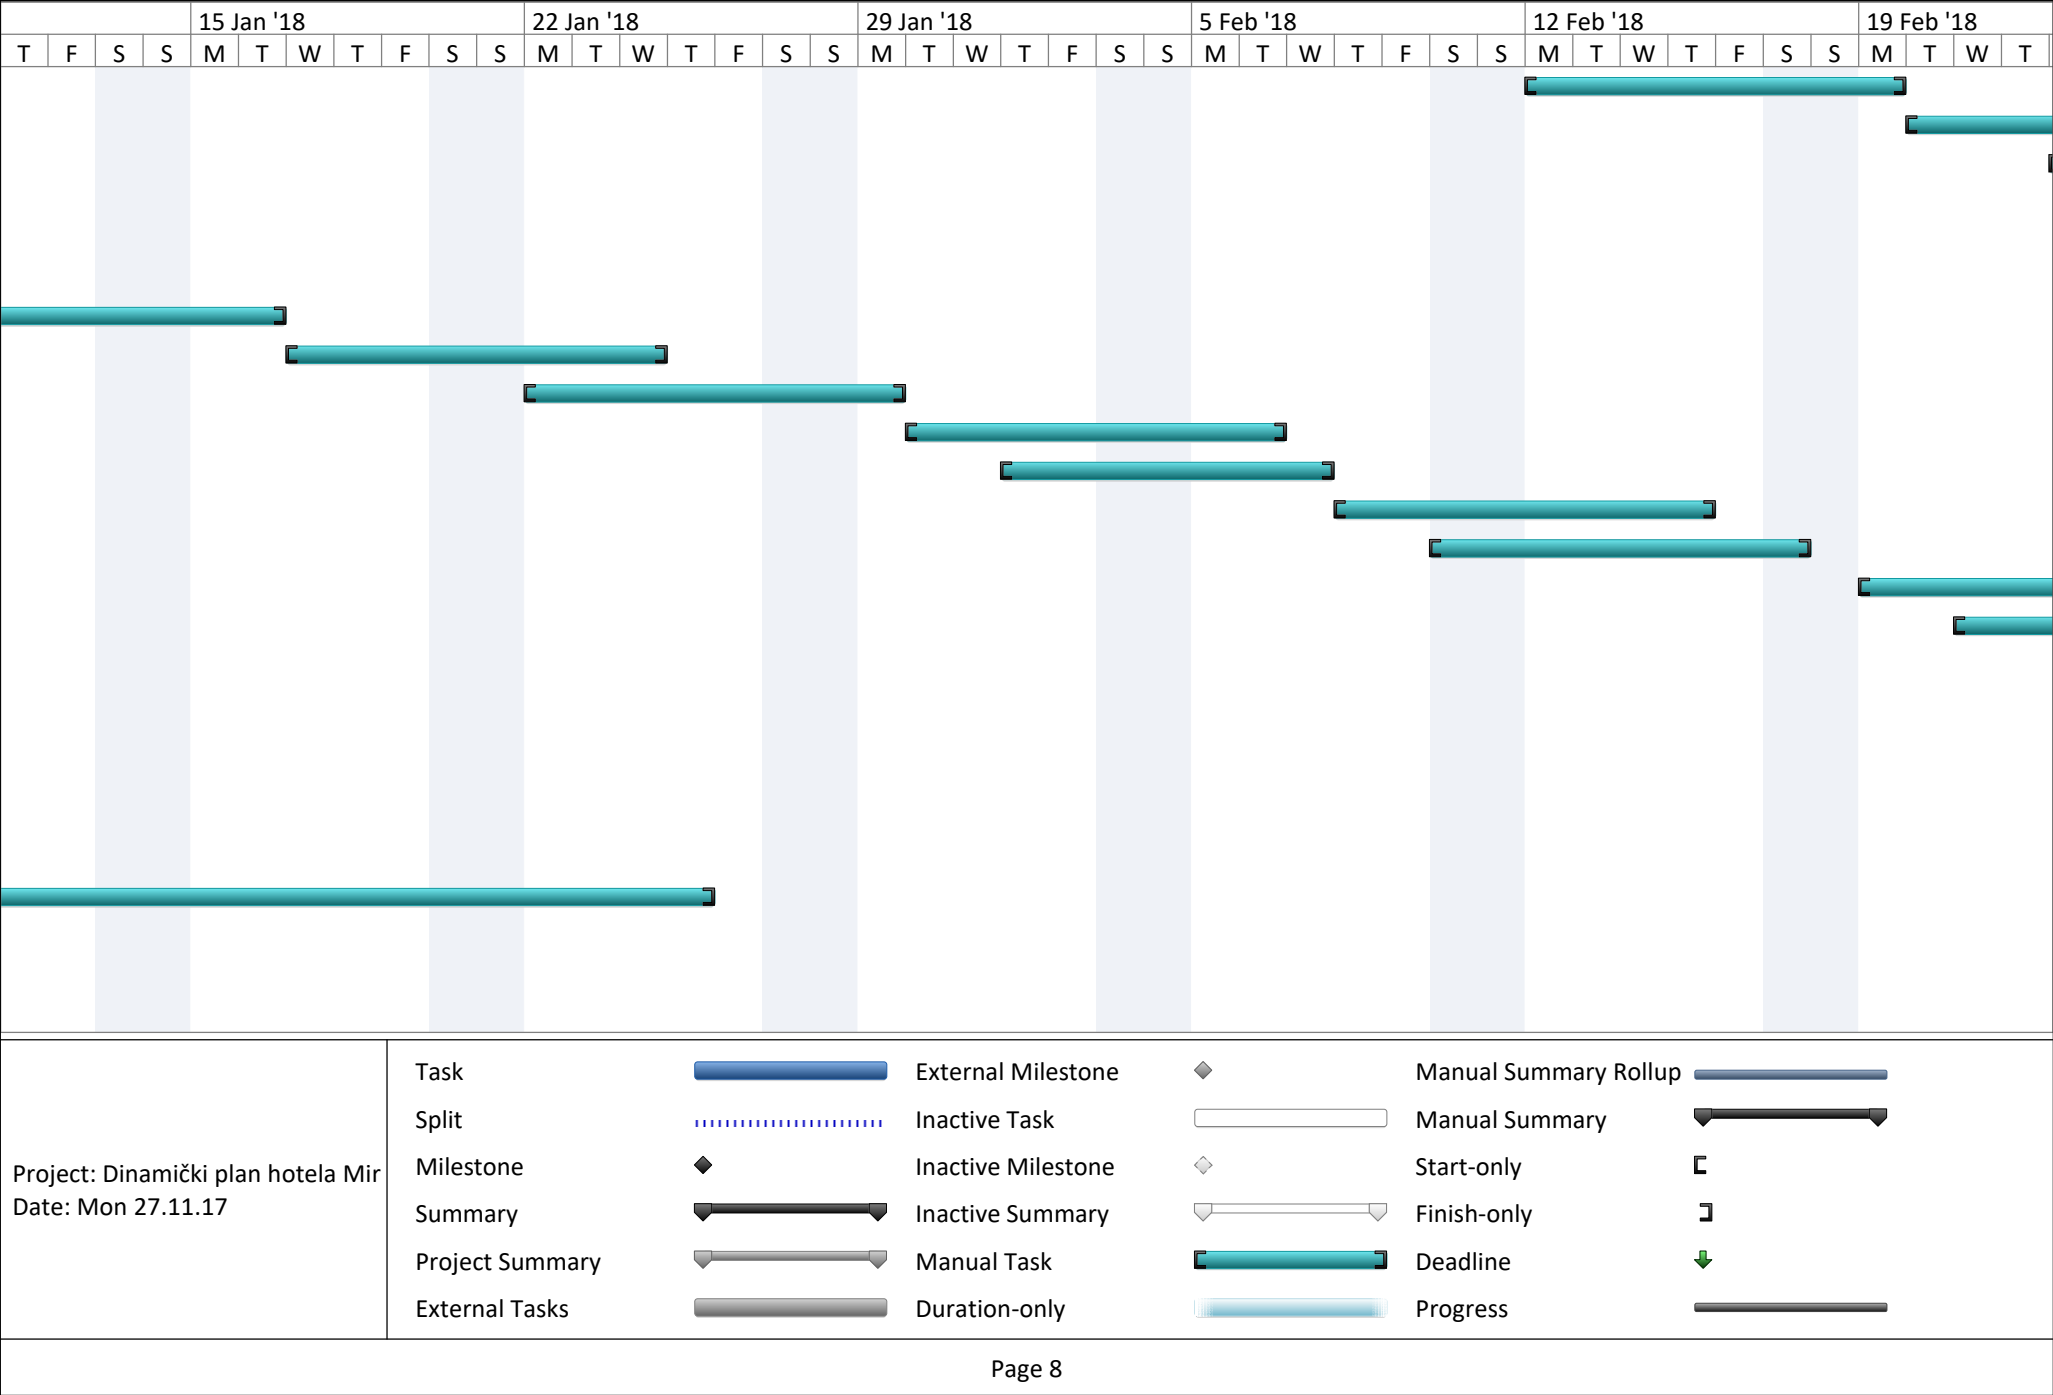

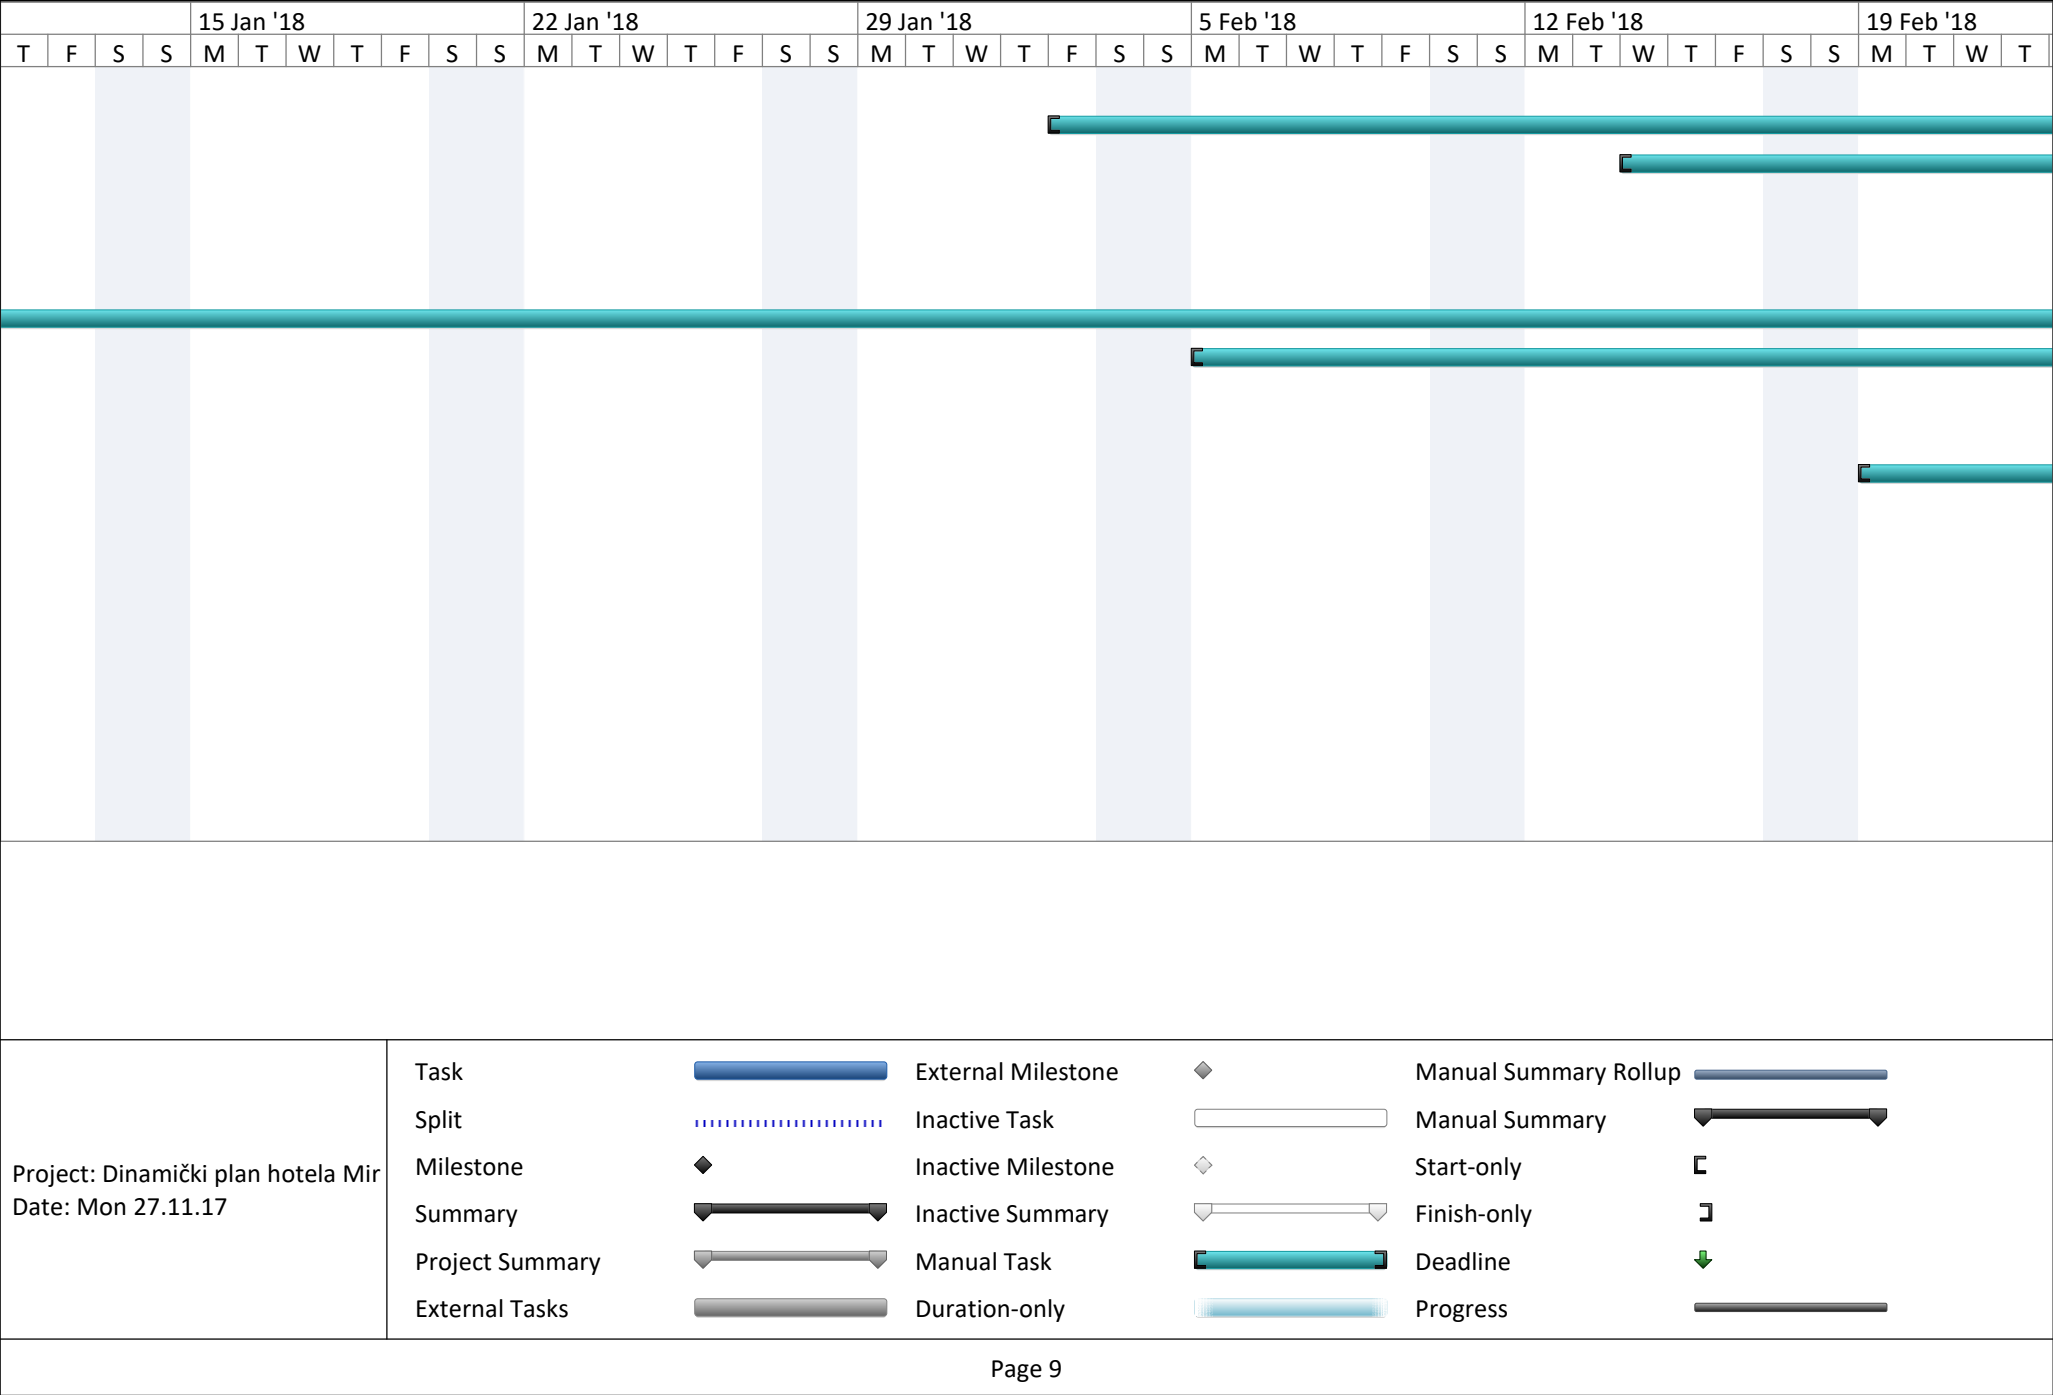

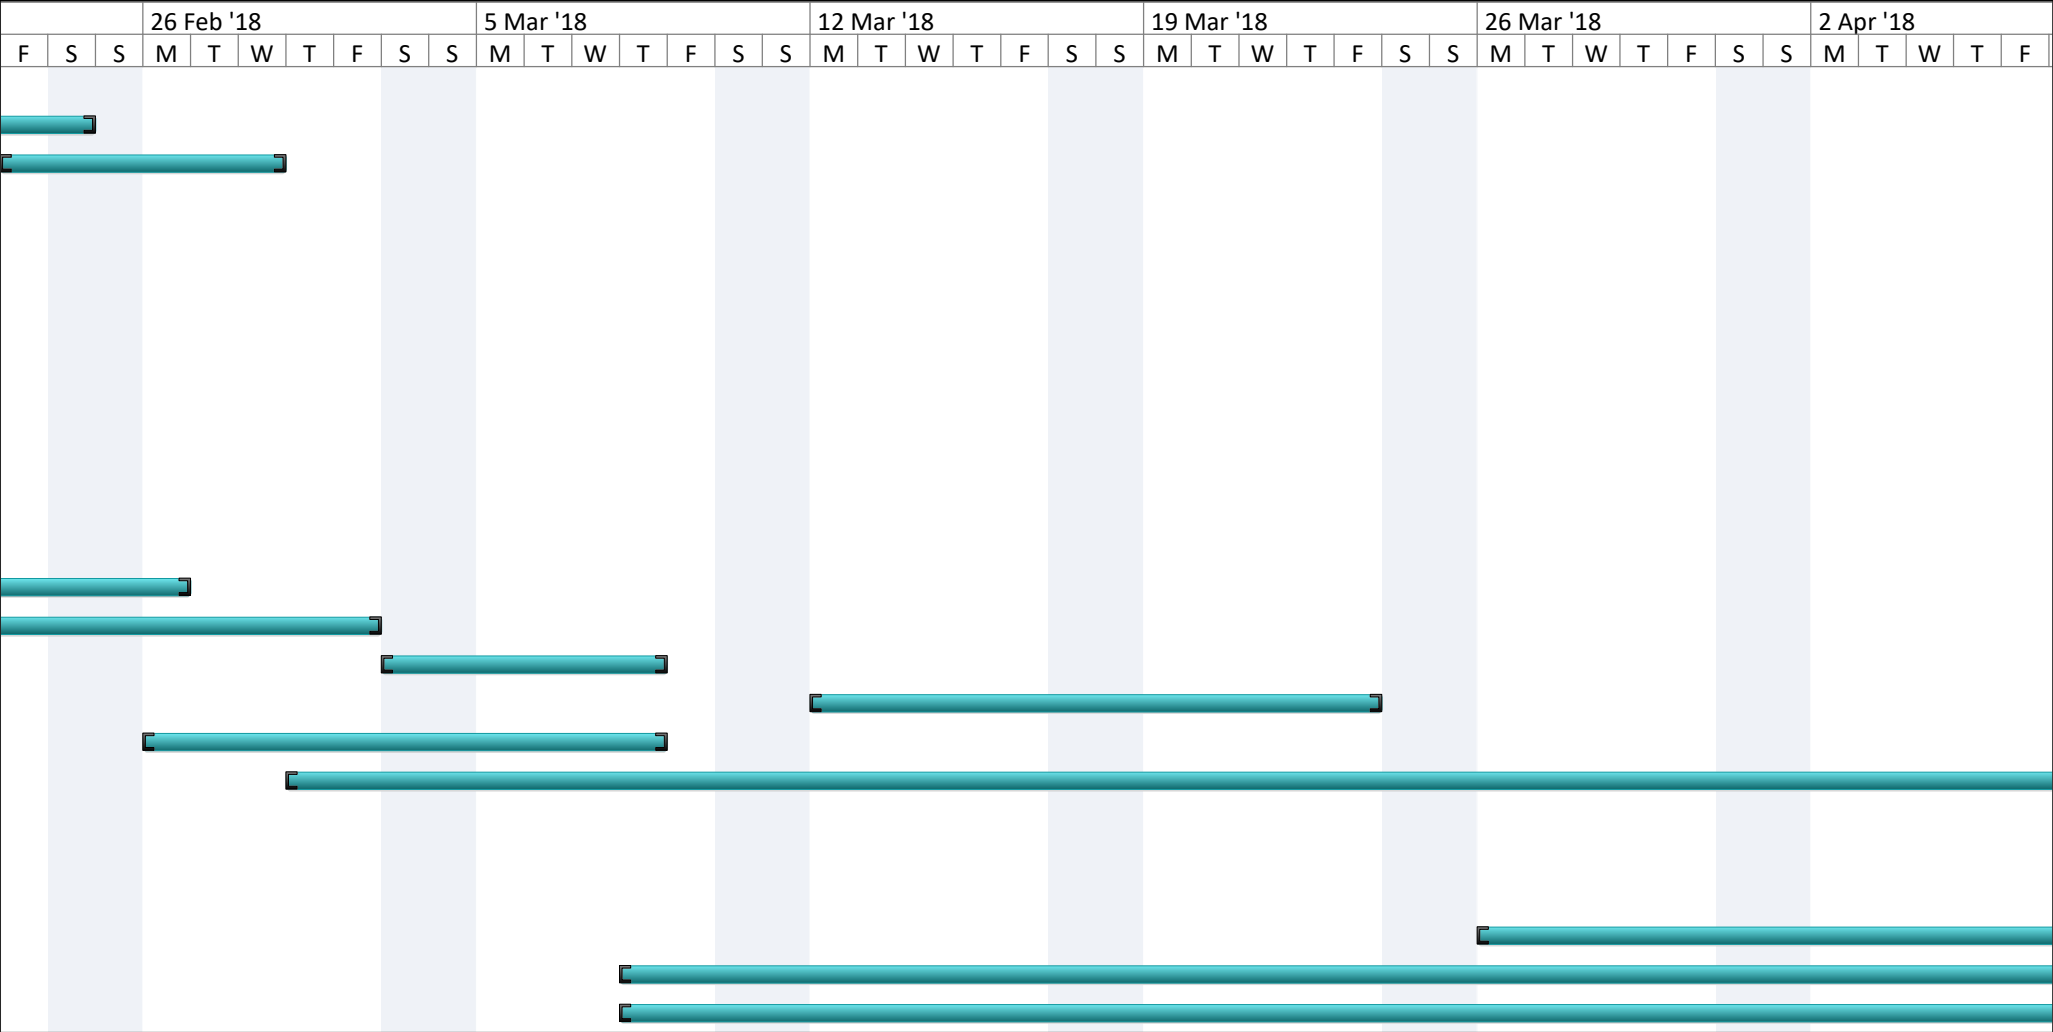

Project: Dinamički plan hotela Mir
Date: Mon 27.11.17

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only


Finish-only

Deadline


Progress

Page 11

		9 Apr '18							16 Apr '18							23 Apr '18							30 Apr '18							7 May '18							14 May '18									
S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S				
Project: Dinamički plan hotela Mir Date: Mon 27.11.17		Task															External Milestone															Manual Summary Rollup														
		Split															Inactive Task															Manual Summary														
		Milestone															Inactive Milestone															Start-only														
		Summary															Inactive Summary															Finish-only														
		Project Summary															Manual Task															Deadline														
		External Tasks															Duration-only															Progress														
Page 13																																														

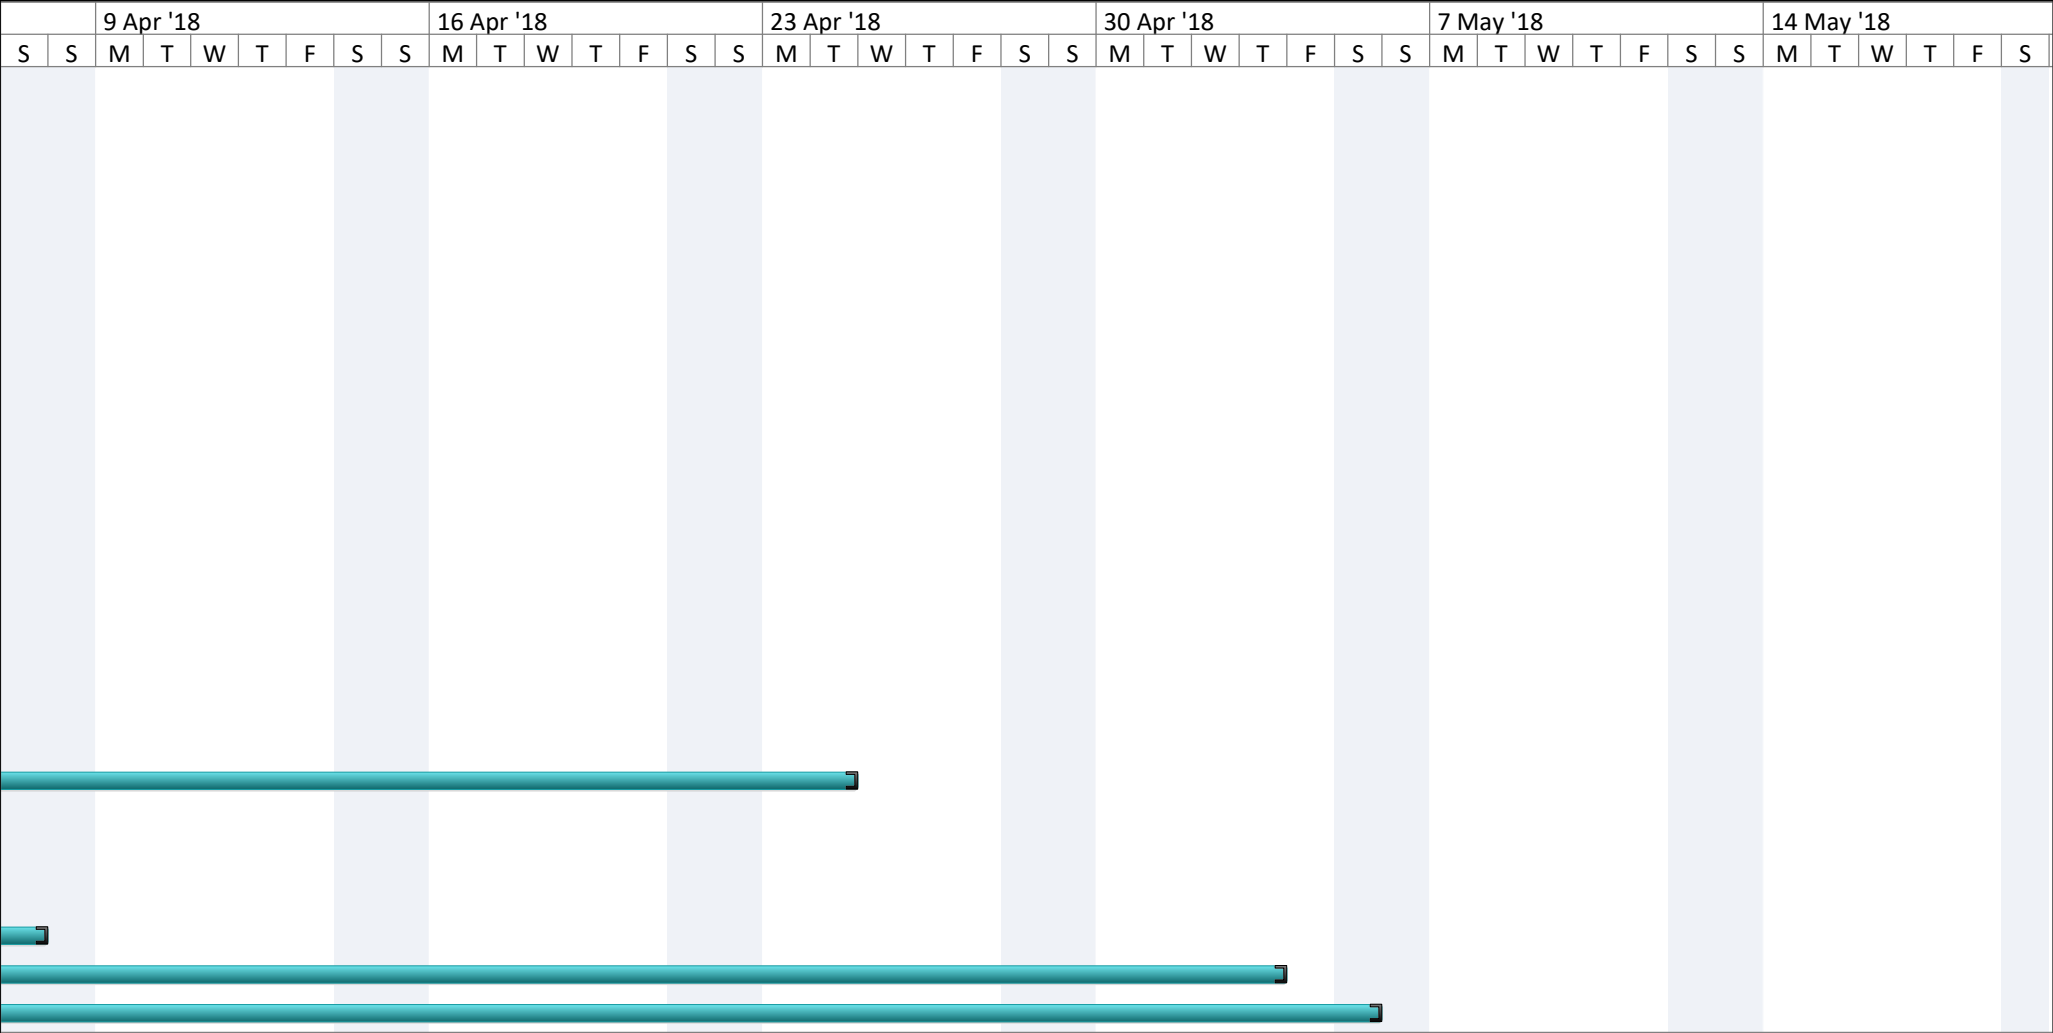

Project: Dinamički plan hotela Mir Date: Mon 27.11.17	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

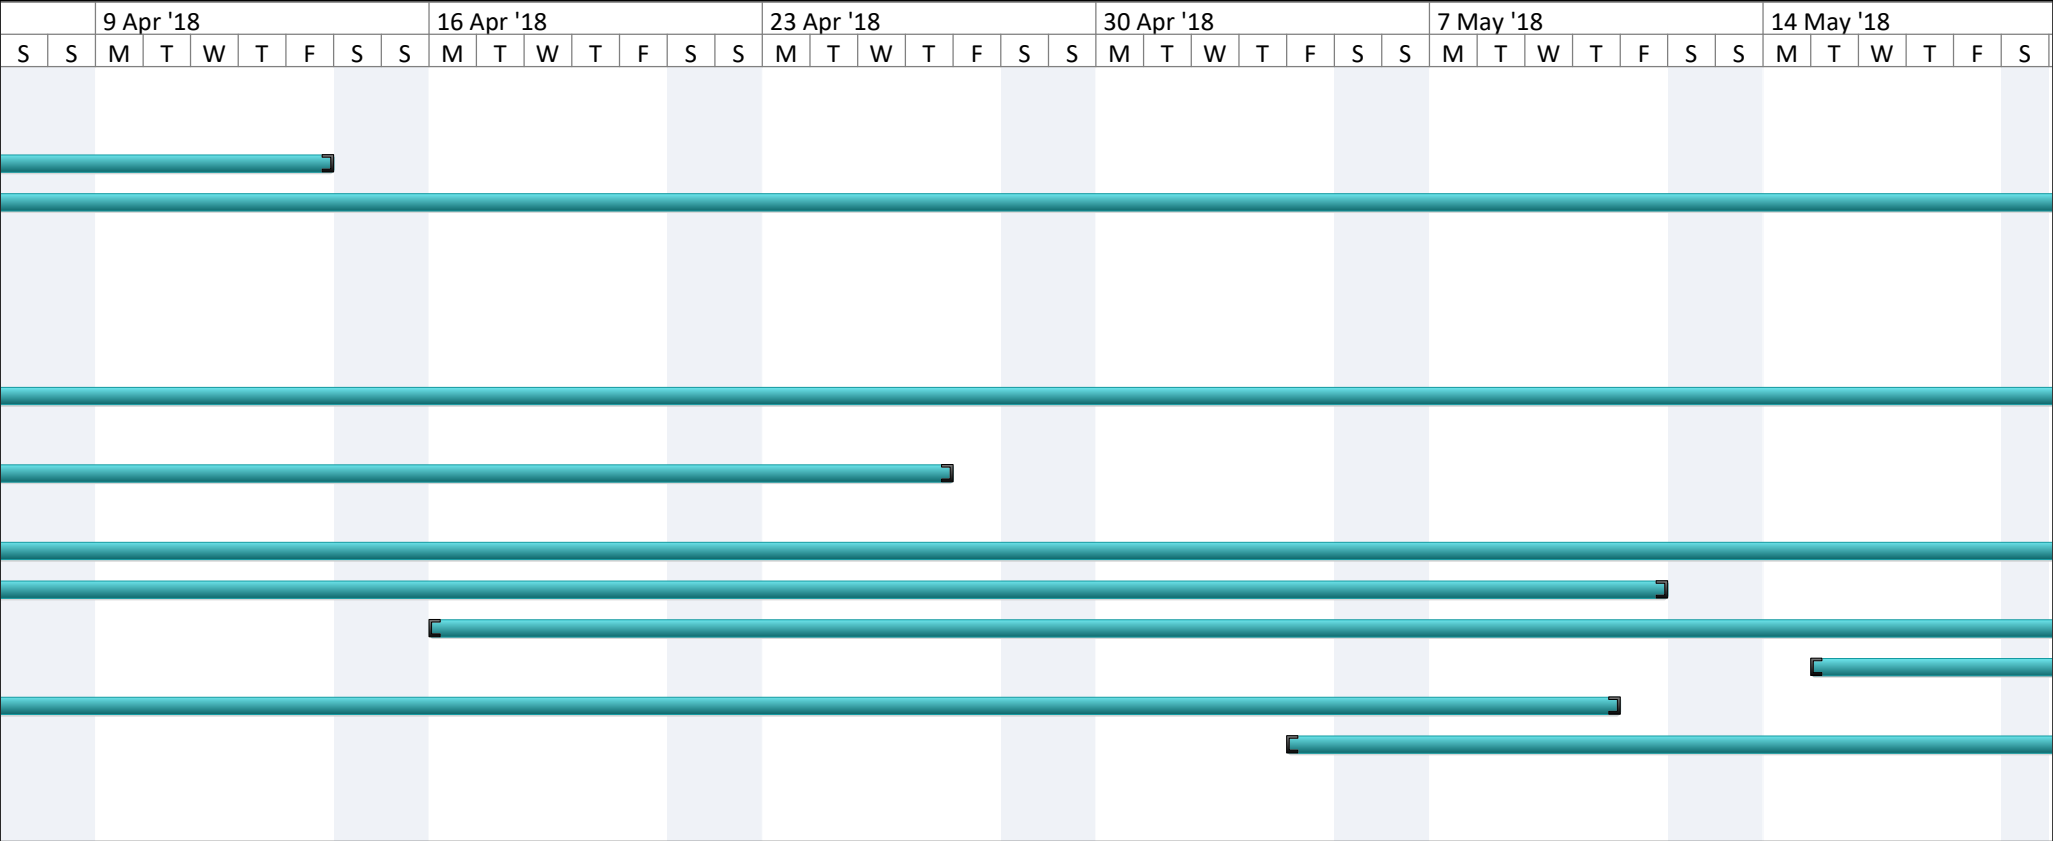

Project: Dinamički plan hotela Mir
Date: Mon 27.11.17

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only


Finish-only

Deadline

Progress

21 May '18							28 May '18							4 Jun '18							11 Jun '18							18 Jun '18							25 Jun '18								
S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	

Project: Dinamički plan hotela Mir Date: Mon 27.11.17	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

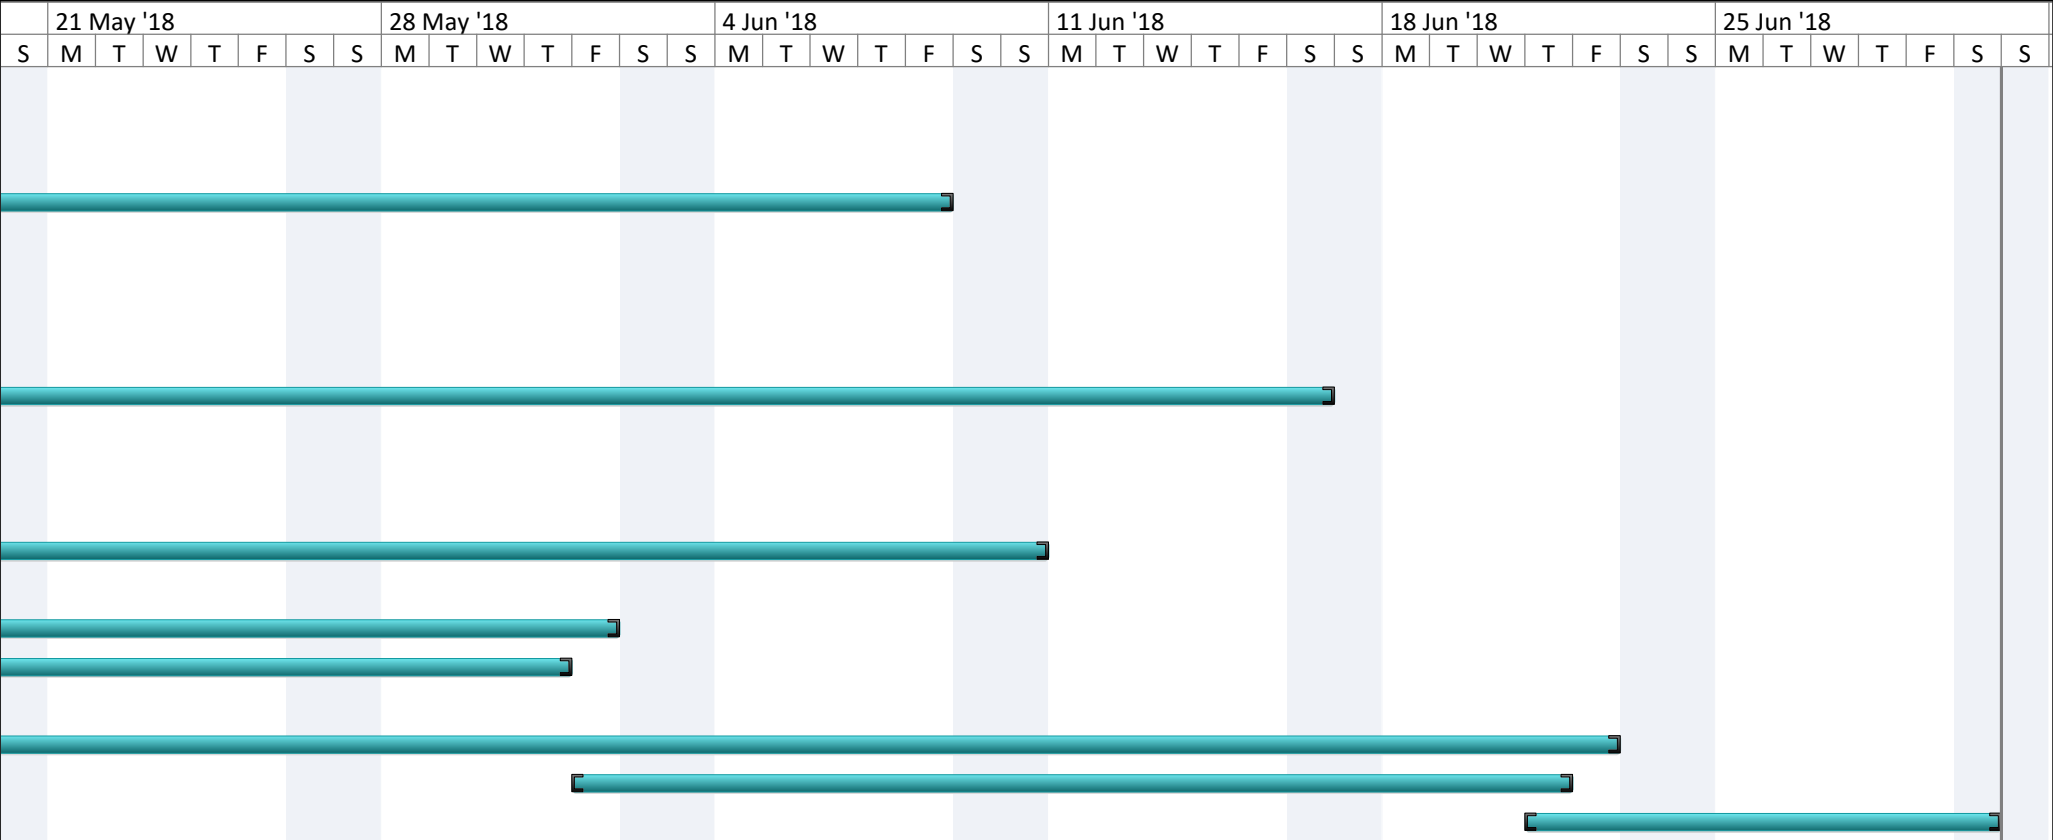

Project: Dinamički plan hotela Mir
Date: Mon 27.11.17

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Progress
